




# MINERAL INSULATED THERMOCOUPLES W/ TERMINAL BLOCK

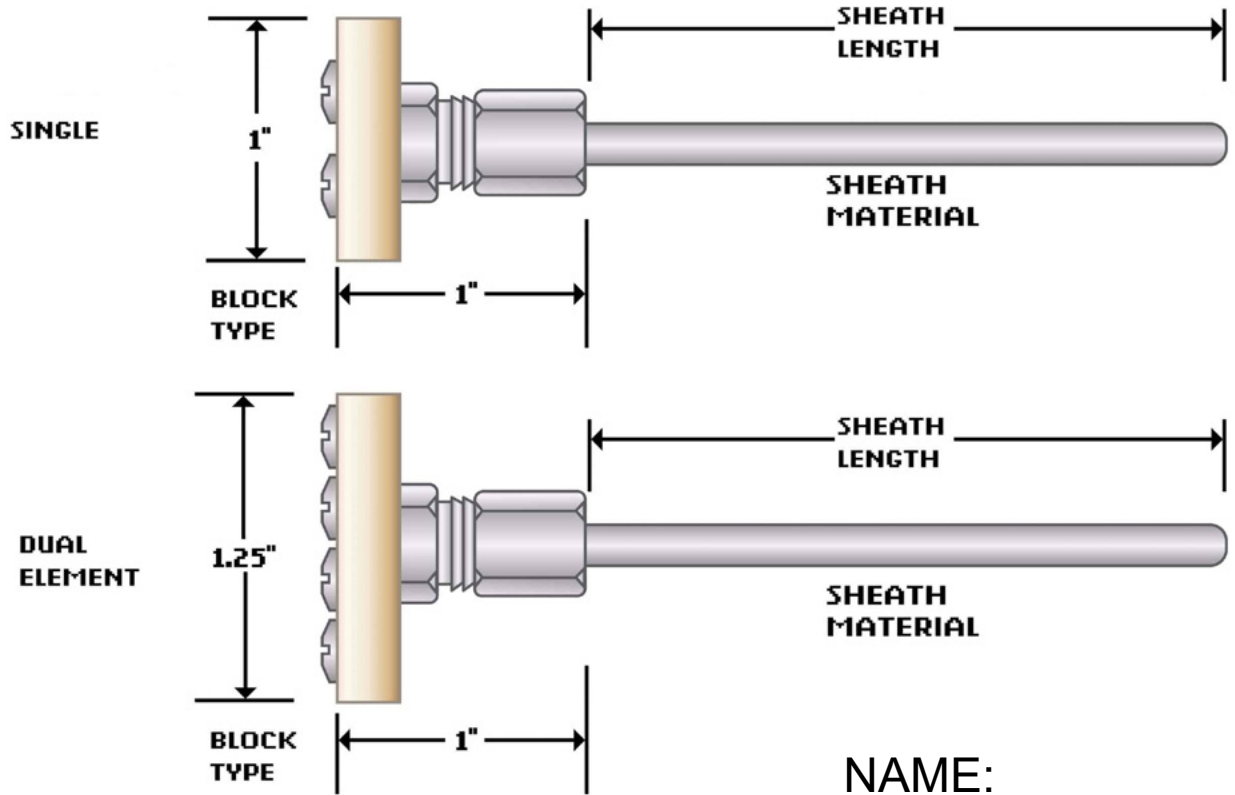

NAME:

## LEAD LENGTH

Length:

Units:

## CALIBRATION

- Type J       Type T       Type J (Dual)       Type T (Dual)  
 Type K       Type E       Type K (Dual)       Type E (Dual)

## SHEATH DIAMETER

- 0.062" (1.6mm)(1/16")  
 0.125" (3.2mm) (1/8")  
 0.188" (4.8mm) (3/16") (standard)  
 0.250" (6.4mm) (1/4")  
 0.314" (8mm) (5/16")  
 0.375" (9.5mm) (3/8")  
 Custom

## SHEATH LENGTH

Length:

Units:

## SHEATH MATERIAL

- 304 SS       310 SS  
 316 SS       Hastelloy  
 Inconel 600  
 446 SS

## JUNCTION

- Grounded  
 Ungrounded  
 Exposed  
 Exposed & recessed

## REQUIRED LEAD TIME

- 1.5-2 weeks (standard)  
 1 week expedited mfg  
 3-4 days expedited mfg  
 1-2 days expedite mfg  
 Same day expedited mfg

## LEAD LENGTH

- Terminal Block

## QUANTITY
